

PROGRESS OF CONSTRUCTION WORK

1. Occupancy is scheduled for Summer 2025.
2. Removal of existing stair complete.
3. Electrical removals, demolition complete

UPCOMING WORK

1. In situ steel and structural elements.
2. Off-site modular construction ongoing, with scheduled completion and arrival on site for January 2025. Please see attached crane plan for information only.

COMMUNITY UPDATE:

Structural works started on site and will continue until January 2025. The modular addition that is being constructed offsite is scheduled to be delivered for early January 2025. The plan is for the modular delivery and crane in place to occur during the holiday break when students are not at school.

Please note that unforeseen circumstances such as weather conditions or authority-imposed delays may affect the timeline. The Capital Services team will keep the school and community informed and will work diligently to minimize any disruptions.

CONSTRUCTION PROGRESS PHOTOS:




3 classrooms being constructed offsite by the Modular Manufacturer

McKee Public School Project Update

Dec 06, 2024



Ongoing on site foundations, footings, and column construction work.

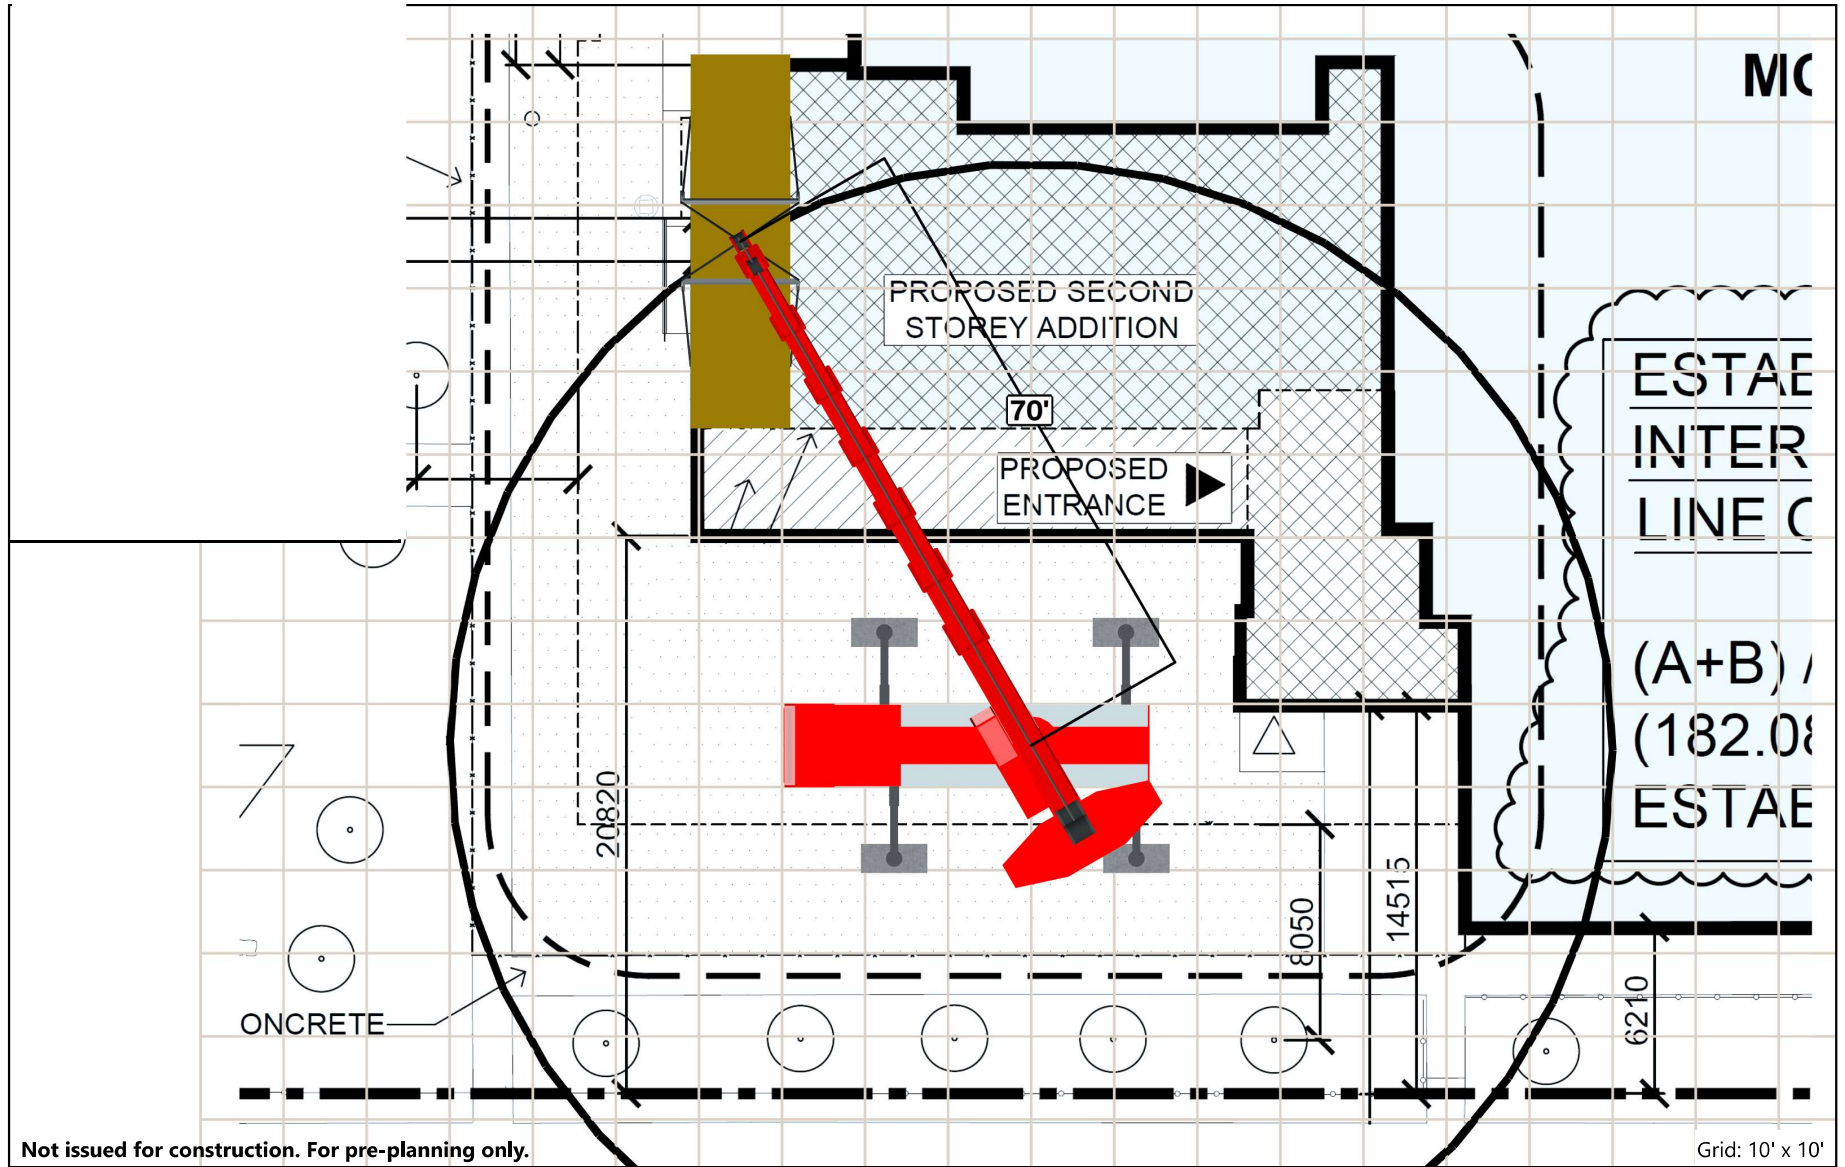

Not issued for construction. For pre-planning only.

Grid: 10' x 10'

Title	Lift Plan
Project	Modular Lift - McKee Public School
Customer	Husky
Description	35 Church Avenue, North York
Drawn By	Chris Welstead
	12/5/2024
