

PROGRESS OF CONSTRUCTION WORK

1. Trinity Construction Management awarded contract to add 3-classroom addition.
2. Occupancy is scheduled for Summer 2025.
3. Trinity mobilized to site and installed construction fencing as of August 12, 2024.
4. Initial demolition works to commence September 3, 2024


UPCOMING WORK

1. Electrical removals, demolition, and rough ins.
2. Inflector demolition.
3. Off-site modular construction commencing, with scheduled completion and arrival on site January

COMMUNITY UPDATE:

Structural and demolition works will begin on site in September and will continue with additional renovation works until January 2025. The modular addition that is to be built offsite is scheduled to be delivered January 2025. The school will be active throughout the full construction period and will be separated by hoarding and appropriate construction signage to ensure there is no impact to ongoing school activities.

CONSTRUCTION PROGRESS PHOTOS:

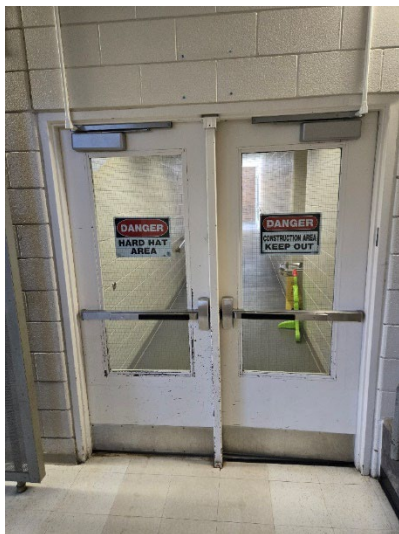

Signage and blocked access to interior construction.



Construction fencing closing in construction area.
